COMPTON COMMUNITY COLLEGE DISTRICT
BOND MASTER PROGRAM SCHEDULE
(JULY 2018 - DECEMBER 2026)
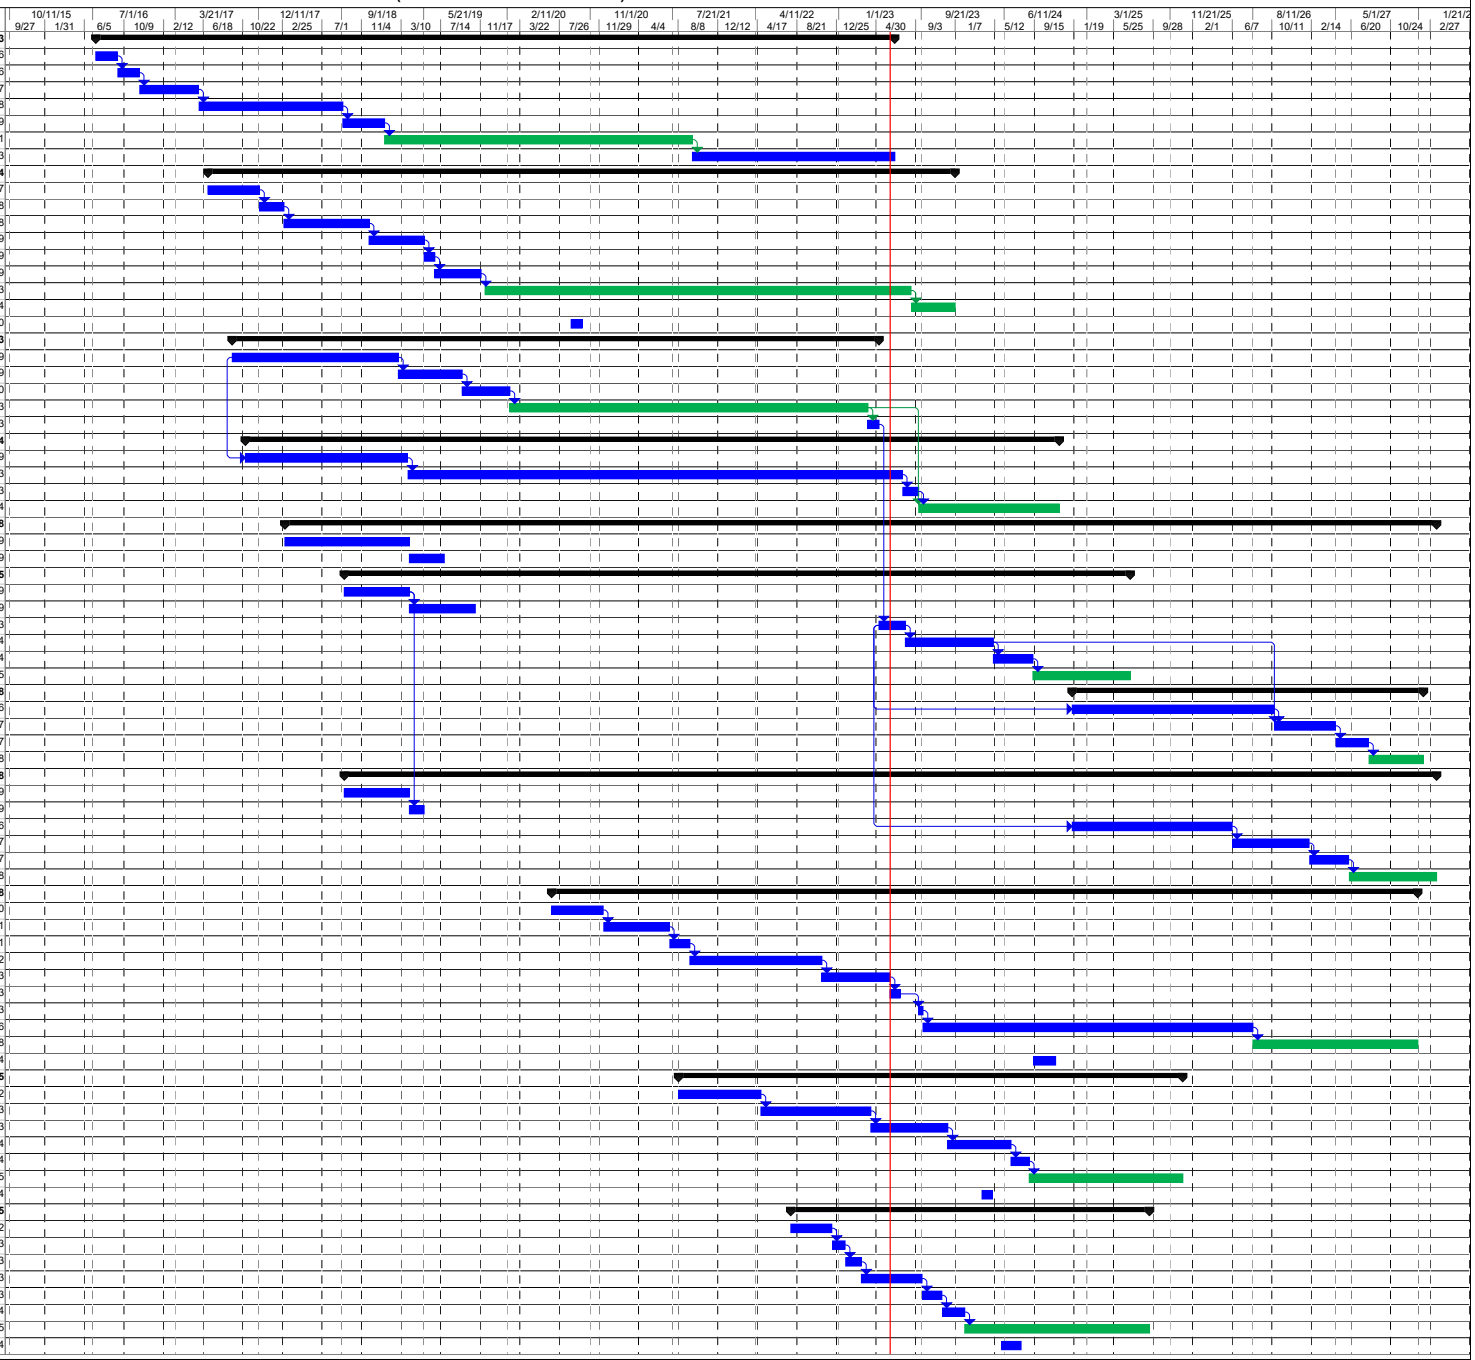
ID	Task Name	Duration	Start	Finish
1	**Instructional Bldg. #1**	**1817 days**	**Mon 7/11/16**	**Tue 6/27/23**
2	District Input	50 days	Mon 7/11/16	Fri 9/16/16
3	Environmental Research	50 days	Mon 9/19/16	Fri 11/25/16
4	Create Bid Documents	135 days	Mon 11/28/16	Fri 6/2/17
5	DSA Approval	327 days	Mon 6/5/17	Tue 9/4/18
6	Bidding/Board Approval/State Approval	95 days	Wed 9/5/18	Tue 1/15/19
7	Construction	700 days	Wed 1/16/19	Tue 9/21/21
8	Close Out, Commissioning, Moving	460 days	Wed 9/22/21	Tue 6/27/23
9	**Instructional Bldg. #2**	**1700 days**	**Mon 7/3/17**	**Fri 1/5/24**
10	Hire Consultants	118 days	Mon 7/3/17	Wed 12/13/17
11	Complete Preliminary Plans	56 days	Thu 12/14/17	Thu 3/1/18
12	Complete Working Drawings (DSA Sub)	193 days	Fri 3/2/18	Tue 11/27/18
13	DSA Approved Drawings	125 days	Wed 11/28/18	Tue 5/21/19
14	State Approval of Plans	24 days	Wed 5/22/19	Mon 6/24/19
15	Bidding/Board Approval/State Approval	105 days	Tue 6/25/19	Mon 11/18/19
16	Construction	970 days	Mon 12/2/19	Fri 8/18/23
17	Demo Bldgs. D, E, & F	100 days	Mon 8/21/23	Fri 1/5/24
18	Advertise bid for FFE	25 days	Tue 9/1/20	Mon 10/5/20
19	**Student Services Bldg.**	**1471 days**	**Mon 9/18/17**	**Mon 5/8/23**
20	Finalize Plans & Specs	379 days	Mon 9/18/17	Thu 2/28/19
21	DSA	145 days	Fri 3/1/19	Thu 9/19/19
22	Bidding & Award	108 days	Fri 9/20/19	Tue 2/18/20
23	Construction	814 days	Wed 2/19/20	Mon 4/3/23
24	MOVING OPERATION	25 days	Tue 4/4/23	Mon 5/8/23
25	**Administration Bldg.**	**1851 days**	**Mon 10/30/17**	**Mon 12/2/24**
26	Finalize Plans & Specs	370 days	Mon 10/30/17	Fri 3/29/19
27	Permits & DSA Approval	1125 days	Mon 4/1/19	Fri 7/21/23
28	Bidding & Award	36 days	Mon 7/24/23	Mon 9/11/23
29	Construction	320 days	Tue 9/12/23	Mon 12/2/24
30	**AOR-RFQ Multiple Buildings**	**2620 days**	**Mon 3/5/18**	**Fri 3/17/28**
31	Arch RFQ/RFP	284 days	Mon 3/5/18	Thu 4/4/19
32	Evaluate & Award AOR Contract	79 days	Fri 4/5/19	Wed 7/24/19
33	**Vo-Tech Renovation**	**1788 days**	**Mon 9/10/18**	**Wed 7/16/25**
34	Arch RFQ/RFP	149 days	Mon 9/10/18	Thu 4/4/19
35	Evaluate & Award AOR Contract	150 days	Fri 4/5/19	Thu 10/31/19
36	Plans & Specs	60 days	Tue 5/9/23	Mon 7/31/23
37	Permits & DSA Approval	200 days	Tue 8/1/23	Mon 5/6/24
38	Bidding & Award	90 days	Tue 5/7/24	Mon 9/9/24
39	Construction	222 days	Tue 9/10/24	Wed 7/16/25
40	**MIS Scope of Work**	**800 days**	**Mon 1/13/25**	**Fri 2/4/28**
41	Plans & Specs	460 days	Mon 1/13/25	Fri 10/16/26
42	Permits & DSA Approval	140 days	Mon 10/19/26	Fri 4/30/27
43	Bidding & Award	75 days	Mon 5/3/27	Fri 8/13/27
44	Construction	125 days	Mon 8/16/27	Fri 2/4/28
45	**Math-Science Renovation**	**2485 days**	**Mon 9/10/18**	**Fri 3/17/28**
46	Arch RFQ/RFP	149 days	Mon 9/10/18	Thu 4/4/19
47	Evaluate & Award AOR Contract	33 days	Fri 4/5/19	Tue 5/21/19
48	Plans & Specs	365 days	Mon 1/13/25	Fri 6/5/26
49	Permits & DSA Approval	175 days	Mon 6/8/26	Fri 2/5/27
50	Bidding & Award	90 days	Mon 2/8/27	Fri 6/11/27
51	Construction	200 days	Mon 6/14/27	Fri 3/17/28
52	**Physical Ed. Complex Replacement**	**1969 days**	**Wed 7/1/20**	**Mon 1/17/28**
53	Hire Consultants	118 days	Wed 7/1/20	Fri 12/11/20
54	Start Preliminary Plans	150 days	Mon 12/14/20	Fri 7/9/21
55	Complete Working Drawings (DSA Sub)	46 days	Mon 7/12/21	Mon 9/13/21
56	DSA Approved Drawings	300 days	Tue 9/14/21	Mon 11/7/22
57	State Approval	155 days	Tue 11/8/22	Mon 6/12/23
58	Advertise Bid for Construction	24 days	Tue 6/13/23	Fri 7/14/23
59	Board Approval - Award	10 days	Tue 9/12/23	Mon 9/25/23
60	Construction Phase 1 - Gym	750 days	Tue 9/26/23	Mon 8/10/26
61	Construction Phase 2 - Pool	375 days	Tue 8/11/26	Mon 1/17/28
62	Advertise bid for FFE	50 days	Thu 9/12/24	Wed 11/20/24
63	**Visual & Performing Arts**	**1147 days**	**Mon 8/9/21**	**Tue 12/30/25**
64	Start Preliminary Plans	188 days	Mon 8/9/21	Wed 4/27/22
65	Start Working Drawings	250 days	Thu 4/28/22	Wed 4/12/23
66	Complete Working Drawings	175 days	Thu 4/13/23	Wed 12/13/23
67	DSA Final Approval	143 days	Thu 12/14/23	Mon 7/1/24
68	Advertise Bid for Construction	42 days	Tue 7/2/24	Wed 8/28/24
69	Construction	349 days	Thu 8/29/24	Tue 12/30/25
70	Advertise Bid for Equipment	25 days	Mon 4/1/24	Fri 5/3/24
71	**Student Housing**	**816 days**	**Mon 8/1/22**	**Mon 9/15/25**
72	Start Preliminary Plans	95 days	Mon 8/1/22	Fri 12/9/22
73	Start Working Drawings	30 days	Mon 12/12/22	Fri 1/20/23
74	Complete Working Drawings	36 days	Mon 1/23/23	Mon 3/13/23
75	DSA Final Approval	139 days	Tue 3/14/23	Fri 9/22/23
76	State Approval	45 days	Mon 9/25/23	Fri 11/24/23
77	Advertise Bid for Construction	51 days	Mon 11/27/23	Mon 2/5/24
78	Construction	420 days	Tue 2/6/24	Mon 9/15/25
79	Advertise Bid for Equipment	45 days	Mon 6/3/24	Fri 8/2/24
